Metropolitan Transportation Commission Programming and Allocations Committee

September 10, 2003

Item Number 4d

State Transportation Improvement Program End-of-Year Project Delivery Status Report (FY 2002-03)

Subject:

End of Fiscal Year 2002-03 project delivery status report for State Transportation Improvement Program (STIP) projects.

Background:

Senate Bill 45 (Chapter 622, Statutes 1997) established strict timely use of funds and project delivery requirements for transportation projects. Projects programmed in the STIP must receive an allocation from the California Transportation Commission (CTC) or Caltrans by the end of the fiscal year in which the funds are programmed. Funds not allocated or extended by the CTC within this deadline are deleted from the STIP with the funds returned to the county in the next county share period.

MTC staff monitors the delivery of STIP projects, and has been informing members of the Bay Area Partnership on a monthly basis of the project delivery requirements and pending deadlines.

Status:

The Bay Area maintained its reputation for on-time project delivery this year for projects programmed in the STIP. Over 91 percent of the programmed projects and 97 percent of the funding were delivered in FY 2002-03, compared with 88 percent of the projects and 96 percent of the funds in FY 2001-02. A chart reflecting the region's STIP project delivery for FY 2002-03 is provided in Attachment A, and summarized below.

A total of 79 projects, for \$209.2 million in Regional Improvement Program (RIP) funds were programmed in FY 2002-03 of the State Transportation Improvement Program (STIP) for the MTC region. Of this amount, 58 projects totaling \$195.2 million received allocations by the June 30, 2003 deadline. The allocation status for each individual STIP project with funds programmed in FY 2002-03 is provided in Attachment B.

An additional sixteen projects totaling \$5.4 million were submitted to Caltrans for allocation. Due to the State's budget situation and the subsequent Allocation Plan instituted by the CTC, these projects were placed on a pending allocation list by the CTC and may be considered for allocation at a later date. These projects are considered delivered under the rules of SB 45. No project needed an allocation extension.

There are seven STIP projects totaling \$6 million with funding in this year that lapsed due to missed allocations. A list of these projects, which represent 9% of the region's projects and 3% of the region's funding programmed in FY 2002-03 of the STIP, is also presented in Attachment A. Of these funds, \$5,100,000 (85% of all lapsed funds) was programmed to the City of Concord's Ygnacio Valley Road Widening Project. The project experienced a significant cost increase and the project was withdrawn from the STIP at the request of the Contra Costa Transportation Authority until additional funding could be secured. These funds will return to the respective county share in the next county share period beginning FY 2004-05.

In addition to the \$195.2 million allocated for the FY 2002-03 projects, \$29.5 million was advanced and allocated for three FY 2003-04 projects:

\$10 Million – Alameda I-680 Soundwalls

\$15 Million – BART Oakland Airport Connector \$4.5 Million – U.S. 101 / Ralston Avenue Interchange Modification


Including these advanced projects, 61 projects, totaling \$224.7 million were allocated in FY 2002-03.

As well, \$26 million programmed in 2002-03 was advanced using local funds through AB 3090 (Statutes of 1992) STIP amendments, which allows project sponsors to advance projects using local funds while receiving a replacement project or reimbursement through the STIP in a later year. Of this \$26 million, \$25 million in local funds was advanced for an Alameda County project, Mission 880 HOV Lanes. Although programmed STIP funds will not be allocated by the CTC until FY 2004-05, the substitution of STIP funds with local funds keeps the projects moving forward and creates up capacity in the CTC's STIP Allocation Plan for additional projects from the MTC region.

Attachments

Attachment A - FY 2002-03 STIP (RTIP) Project Delivery Status Chart Attachment B - List of STIP projects programmed in FY 2002-03 with status

MTC Region FY 2002-03 End of Year Local and Caltrans RTIP Project Delivery as of June 30, 2003

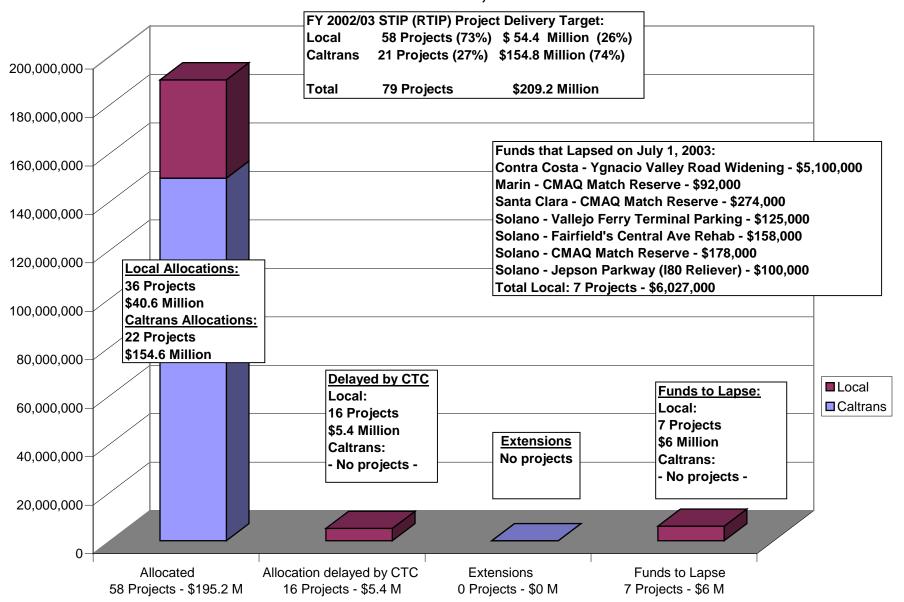

STIP ALLOCATION STATUS REPORT ALLOCATION DEADLINE 6/30/2003 ALAMEDA COUNTY

ALAMEDA COUNTY RTIP

TIP ID	Agency	Project	Allocation Date Phase	Programmed Amount	Completed Allocations	Balance Comments
ALA990020	AC Transit	Engine transmission rehab	CON	628,000	0	*On CTC pending allocation list; below current allocation plan line - allocation not anticipated in 628,000 near future
ALA010003	Alameda Co	Crow Cyn Rd, improvements	PSE	450,000	0	Removed from STIP in June 03 - AB 3090 450,000 replacement project in FY 04-05
ALA990010	Caltrans	EB HOV lane ext at Bay Bridge	6/13/2002 CON	4,895,000	4,895,000	0 Allocated
ALA978027	Caltrans	HOV, SCI Co Line-Alvarado/Niles	6/26/2003 CON	33,960,000	8,923,000	-, , ,
			PSE &			Allocated
ALA010006	Caltrans	Extend Dumbarton HOV Ins to Rt 880	7/1/2002 ENV	480,000	,	0 PSE 375,000; ENV 105,000
ALA010005	Caltrans	HOV on ramp at Newark BI	7/1/2002 PSE	300,000	300,000	0 Allocated
ALA010009	Caltrans	Soundwall, Livermore, Vasco Rd-First St	7/1/2002 ROW	73,000	73,000	0 Allocated
ALA010032	Caltrans	Rt 580 noise barrier	7/1/2002 PSE	600,000	600,000	0 Allocated
ALA010050	Caltrans	Soundwall, Oakland EB, 14th Av-Ardley	ENV & PSE & 7/1/2002 RW SUP	122,000	122.000	Allocated 0 ENV 39,000: PSE 73,000; ROW SUP 10,000
MTC990005	MTC	PPM (SO)	9/16/2002 CON	86,000	86,000	0 Allocated
ALA99SA01	ACCMA	PPM (SO)	10/21/2002 CON	100,000	100,000	0 Allocated
ALA010052		Central Ave RR overpass at UPRR	ENV	145,000	•	Removed from STIP in June 03 - AB 3090 145,000 replacement project in FY 04-05
ALA010053	Newark	Thornton Av, Gateway-Hickory, widen	ENV	120,000	0	Removed from STIP in June 03 - AB 3090 120,000 replacement project in FY 04-05
ALA99SA18	Union City	Alvarado-Niles, pavement rehab	CON	240,000	0	Removed from STIP in June 03 - AB 3090 240,000 replacement project in FY 04-05
TOTAL 0.50		M COLINTY DTID		40.400.000	45 570 000	20.000.000

TOTALS FOR ALAMEDA COUNTY - RTIP

42,199,000 15,579,000 26,620,000

TIP ID	Agency	Project	Allocation Date	Phase	Programmed Amount	Completed Allocations	Balance	Comments
				ROW &				
ALA977048	Fremont	Capitol Corridor Centerville Station	5/22/2003	CON	1,205,000	1,205,000	0	Allocated ROW 855,000; CON 350,000
TOTALS FO	R ALAMEDA	COUNTY - ITIP			1,205,000	1,205,000	0	

STIP ALLOCATION STATUS REPORT ALLOCATION DEADLINE 6/30/2003 CONTRA COSTA COUNTY

CONTRA COSTA RTIP

TIP ID	Agency	Project	Allocation Date Pha	Programmed ase Amount	Completed Allocations	Balance C	omments
CC-990004	Caltrans	HOV In, Marina Vista-N Main	6/13/2002 CON	, ,	32,696,000	0 Allocated	
CC-990007	Caltrans	Rt. 4 Widening - RR Ave. to Loveridge Rd.	CON CON 5/22/2003 SUP		22,707,000	0 Allocated CON 19,307,00	00: CON SUP 3.400.000
CC-99SA08	Caltrans	Alcosta Rd interchange	6/26/2003 CON	3,500,000	0	3,500,000 Allocated	.,
CC-010001	Concord	Ygnacio Valley Rd widening	CON	5,100,000	0	5,100,000 * Funds lapsed	
MTC990005	MTC	Planning, programming, and monitoring (SO)	9/16/2002 CON	54,000	54,000	0 Allocated	
CC-010024	Antioch	Rt 4 Hillcrest Av EB off ramp, widen	ENV	50,000	0	*On CTC pending allocat 50,000 plan line - allocation not a	ion list; below current allocation
CC-010025	ACCMA	San Pablo Ave SMART corridor	8/22/2002 CON	1,500,000	1,500,000	0 Allocated	
CC-991089	Lafayette	Reliez Valley Rd walkway (SO)	CON	109,000	0	*On CTC pending allocat 109,000 plan line - allocation not a	ion list; below current allocation
CC-010033	Danville	Oak Hill Park frontage improvements (SO)	CON	62,000	0	*On CTC pending allocat 62,000 plan line - allocation not a	ion list; below current allocation anticipated in near future
CC-010035	CC Count	y Stone Valley Rd W sidewalk to Ironhorse Trail (SO)	ENV 7/18/2002 PSE	& 14,000	4,000	ENV 4,000; PSE 10,000 below current allocation p 10,000 anticipated in near future	On CTC pending allocation list lan line - allocation not
CC-010036	San Pablo	San Pablo Dam Rd ped path (SO)	CON	115,000	0	*On CTC pending allocat 115,000 plan line - allocation not a	ion list; below current allocation
CC-010038	CC Count	y I-80 Bikeway storm drain grates (SO)	ENV 9/1/2002 PSE	& 5,000	3,000	ENV 3,000; PSE 2,000 C below current allocation p 2,000 anticipated in near future	
CC010040	Martinez	Bay Trail, phase 2 segments (SO)	ROW CON		0		,000 On CTC pending allocation on plan line - allocation not
CC-010027	BART	Pittsburg-Bay Point terminal zone, turnback	PSE	350,000	0	·	ted for CON funds and moved plan line; these PSE funds are plan line - allocation not
CC-010030	BART	Add parking level @ Richmond BART station	PSE	200,000	0	•	ted; funds are below current ation not anticipated in near
				,	_		
ITIP	R CONTRA	COSTA COUNTY - RTIP		66,762,000	56,964,000	9,798,000	
TIP ID	Agency	Project	Allocation Date Pha	Programmed se Amount	Completed Allocations	Balance C	omments
CC-990007	Caltrans	Rt. 4 Widening - RR Ave. to Loveridge Rd.	5/22/2003 CON	5,000,000	5,000,000	0 Allocated	
CC-010003	Caltrans	I-80 WB HOV GAP Closure	ROW ROW 7/1/2002 SUP		1,500,000	Allocated (Caltrans Support) 0 ROW 1,300,000; ROW SUP	200.000
			7, 1,2002 301	, ,			,
TOTALS FO	R CONTRA	COSTA COUNTY - ITIP		6,500,000	6,500,000	0	

STIP ALLOCATION STATUS REPORT ALLOCATION DEADLINE 6/30/2003 MARIN COUNTY

MARIN COUNTY RTIP

			Allocation		Programmed	Completed		
TIP ID	Agency	Project	Date	Phase	Amount	Allocations	Balance	Comments
		·						
				00110				
				CON &				artial Allocation - \$5,975,000 moved to FY 03-04
MRN990001	Caltrans	Reversible HOV, segs 2,3,4	6/26/2003	CON SUP	8,000,000	2,025,000	5,975,000 C	ON 6,441,000; CON SUP \$1,559,000
							*	23,000 *On CTC pending allocation list;
							b	elow current allocation plan line -
							F	Remaining \$92,000 lapses - returned to
MTC990004	MTC	CMAQ match reserve (SO)		CON	115,000	0	115,000 N	Marin County Share
MTC990003	MTC	Regional rideshare program (SO)	9/17/2002	CON	100,000	100,000	0 A	llocated
MTC990005	MTC	PPM (SO)	9/16/2002	CON	18,000	18,000	0 A	Illocated
MRN991006	Larkspur	Sir Francis Drake BI, Rt 101-east limits (SO)	9/12/2002	CON	163,000	163,000	0 A	Illocated
							C	CON 121,000; PSE 10,000
							*	On CTC pending allocation list; below
				PSE &				urrent allocation plan line - allocation not
MRN010027	Sausalito	Bridgeway, Princess-Johnson, rehab (SO)	4/3/2003		131,000	0		nticipated in near future
MRN990035	Marin CM/	A Manzanita park and ride, phase 2 (SO)	6/26/2003	CON	311,000	0	311,000 A	Illocated
TOTALS FOR	MARIN CO	DUNTY - RTIP			8,838,000	2,306,000	6,532,000	

TIP ID	Agency	Project	Allocation Date	Phase	Programmed Amount	Completed Allocations	Balance	Comments
MRN990001	Caltrans	Reversible HOV, segs 2,3,4	6/26/2003	CON	7,000,000	7000000	0 Allocated	
TOTALS FOR	MARIN CO	UNTY - ITIP			7,000,000	7000000	0	

STIP ALLOCATION STATUS REPORT ALLOCATION DEADLINE 6/30/2003 NAPA COUNTY

NAPA COUNTY RTIP

			Allocation		Programmed	Completed		
TIP ID	Agency	Project	Date	Phase	Amount	Allocations	Balance	Comments
MTC990005	MTC	Planning, programming, and monitoring (SO)	9/16/2002	CON	10,000	10,000	0 Allo	cated
NAP010007	Napa County	Steele Canyon Rd, Rt 128-Headlands, rehab (SO)	7/16/2002	CON	450,000	450,000	0 Allo	cated
NAP010009	Napa TPA	Planning, programming, and monitoring (SO)	4/3/2003	PSE	60,000	60,000	0 Allo	cated
TOTALS FOR	NAPA COUNT	TY - RTIP			520,000	520,000	0	

ITIP

TOTALS FOR NAPA COUNTY - ITIP

STIP ALLOCATION STATUS REPORT ALLOCATION DEADLINE 6/30/2003 SAN FRANCISCO COUNTY

SAN FRANCISCO COUNTY RTIP

			Allocation		Programmed	Completed		
TIP ID	Agency	Project	Date	Phase	Amount	Allocations	Balance	Comments
MTC990003	MTC	Regional rideshare program (SO)	9/17/2002	CON	322,000	322,000	0 Alloca	ited
SF-010008	MTC/SFCTA	Planning, programming, and monitoring (SO)	5/22/2003	CON	58,000	58,000	0 Alloca	ited
MTC990005	MTC	Planning, programming, and monitoring (SO)	9/16/2002	CON	47,000	47,000	0 Alloca	ited
SF-991030	Caltrans	Doyle Dr replace		PSE	8,000,000	5,000,000	3,000,000 *Ame	ndment shifted \$3m to ENV
SF-010030	San Francisco	Laguna Honda, O'Shaughnessy bike paths (SO)	11/15/2002	PSE	160,000	160,000	0 Alloca	ited
SF-010027	Peninsula JPB	Caltrain rapid rail improvements	5/22/2003	CON	3,000,000	3,000,000	0 Alloca	ited
							below	TC pending allocation list; current allocation plan line - tion not anticipated in near
SF-010029	BART	Embarcadero, Montgomery seismic retro (SO)		ENV	500,000	0	500,000 future	
TOTALS FOR SAN FRANCISCO COUNTY RTIP 12,087,000 8,587,000 3,500,000								

TIP ID	Agency	Project	Allocation Date	Phase	Programmed Amount	Completed Allocations	Balance	Comments
SF-991030	SFCTA	SR 101 Doyle Drive Replacement	7/1/2002 PS	SE	28,000,000	28,000,000	0	Allocated (Caltrans Support)
TOTALS FO	R SAN FRAN	ICISCO COUNTY - ITIP			28,000,000	28,000,000	0	

STIP ALLOCATION STATUS REPORT ALLOCATION DEADLINE 6/30/2003 SAN MATEO COUNTY

SAN MATEO COUNTY RTIP

			Allocation		Programmed	Completed		
TIP ID	Agency	Project	Date	Phase	Amount	Allocations	Balance	Comments
SM-010031	Caltrans	Aux lanes, 3rd Av-Millbrae Av	07/01/02	PSE	350,000	350,000	0 Allocate	ed
SM-010009	Atherton	Middlefield Rd. Rehabilitation	01/02/02	CON	152,000	152,000	0 Allocate	ed
MTC990005	MTC	Planning, programming, and monitoring (SO)	09/16/02	CON	47,000	47,000	0 Allocate	ed
,				ENV &			Allocat	ed
SM-010046	Caltrans	Aux lanes-SCL Co. line to Marsh Rd	07/01/02	PSE	1,535,000	1,535,000	0 ENV 50	3,000; PSE 1,482,000
				ENV &			Allocate	ed
SM-010047	Caltrans	Willow Rd interchange reconstruction	07/01/02	PSE	1,029,000	1,029,000	0 ENV 54	I,000; PSE 975,000
SM-010005	BART	SFO Airport Bicycle Trail (SO)		PSE ROW & CON	1,500,000	157,000	below o allocati future.	C pending allocation list; current allocation plan line - on not anticipated in near 57,000; 655,000 ROW; O CON
MTC990003	MTC	Regional rideshare program (SO)	09/17/02	CON	265,000	265,000	0 Allocate	ed
TOTALS FOR	SAN MAT	EO COUNTY			4,878,000	3,535,000	1,343,000	

TIP ID	Agency	Project	Allocation Date	Phase	Programmed Amount	Completed Allocations	Balance	Comments
SM-010031	Caltrans	SR 101 Auxiliary Lanes - 3rd to Millbrae		PSE & ROW SUP	239,000	239.000	0	Allocated (Caltrans Support) PSE 199,000; ROW SUP 40,000
TOTALS FOR	R SAN MATE	0	•					

STIP ALLOCATION STATUS REPORT ALLOCATION DEADLINE 6/30/2003 SANTA CLARA COUNTY

SANTA CLARA COUNTY RTIP

					Programmed	Completed		
TIP ID	Agency	Project	Allocation Date	Phase	Amount	Allocations	Balance	Comments
SCL990041	Caltrans	Guadalupe Pkwy	6/13/2002 (CON	27,303,000	27,303,000	0 All	ocated
								wo projects (292K and 231K)
								CTC pending allocation list;
							be	ow current allocation plan
							lin	e - allocation not anticipated
							in	near future. \$274,000 lapsed
MTC990004	MTC	CMAQ match reserve (SO)	(CON	1,131,000	334,000	797,000 an	d returned to county share
JPB991001	JPB Caltrain	Diridon station, platform, track work	6/22/2003 (CON	2,606,000	2,606,000	0 All	ocated
MTC990003	MTC	Regional rideshare program (SO)	9/17/2002 (CON	136,000	136,000	0 All	ocated
MTC990005	MTC	PPM (SO)	9/16/2002 (CON	102,000	102,000	0 All	ocated
							CC	N 1,144,000; CON SUP
							15	6,000 This allocation splits
			(CON & CON				
SCL010022	Caltrans	Rt 87-Trimble Rd, aux lane	6/22/2003	SUP	1,300,000	1,112,000		livery in FY 2005-06
SCL010007	SCVTA	Rt 237/880 improvements, stage C	7/18/2002(CON	22,500,000	22,500,000	0 All	ocated
SCL010004	MTC/SCVTA	PPM (SO)	6/22/2003 (CON	291,000	291,000	0 All	ocated
TOTALS FOR	R SANTA CLA	RA COUNTY - RTIP			55,369,000	54,384,000	985,000	
SCL010007 SCL010004	SCVTA MTC/SCVTA	Rt 237/880 improvements, stage C PPM (SO)	6/22/2003 \$ 7/18/2002 (CON	22,500,000 291,000	22,500,000 291,000	off 188,000 de 0 All 0 All	a landscaping project for livery in FY 2005-06 ocated

TIP ID	Agency	Project	Allocation Date	Phase	Programmed Amount	Completed Allocations	Balance	Comments	
SCL010022	Caltrans	US 101 Aux Lane from SR 87 to Trimble		ROW CON & CON SUP	18,000,000	13,150,000		ROW 2,625,000; CON 13,531,000, CON SUP 1,844,000 This allocation splits off a landscaping project for delivery in FY 2005-06	
TOTALS FOR SANTA CLARA COUNTY - ITIP 18,000,000 13,150,000 4,850,000									

STIP ALLOCATION STATUS REPORT ALLOCATION DEADLINE 6/30/2003 SOLANO COUNTY

SOLANO COUNTY RTIP

			Allocation	Programmed	Completed		
TIP ID	Agency	Project	Date Phase	Amount	Allocations	Balance	Comments
MTC990003	MTC	Regional rideshare program (SO)	9/17/2002 CON	155,000	155,000	0 Allocated	
						Lap	sed and returned to Solano
MTC990004	MTC	CMAQ match reserve (SO)	CON	178,000	0	178,000 Cou	nty share
MTC990005	MTC	Planning, programming, and monitoring (SO)	9/16/2002 CON	26,000	26,000	0 Allo	cated
							sed and returned to Solano
SOL950035	Vallejo	Vallejo ferry terminal parking	ENV	125,000	0	125,000 Cou	nty share
SOL990004	Solano TA	Jepson Parkway (I-80 reliever)	ENV & 4/3/2003 ROW	300,000	200,000	\$20	/ 200,000; ROW 100,000 0,000 Obligated *\$100,000 ed and returned to Solano nty share
SOL991038	Fairfield	Air Base Pkwy, Peabody-Main Gate Travis, overlay	10/21/2002 CON	645,000	645,000	0 Allo	
SOL010013	Fairfield	Central Way, Ritchie-Pitman, overlay	4/3/2003 CON	158,000	0		sed and returned to Solano
SOL991039	Fairfield	N Texas St, Travis Bl-Air Base Pkwy, overlay	6/10/2002 CON	362,000	362,000	0 Allo	cated
SOL010002	MTC/STA	Planning, programming, and monitoring (SO)	9/19/2002 CON	214,000	214,000	0 Allo	cated
TOTALS FOR SOLANO COUNTY				2,163,000	1,602,000	561,000	

TIP ID	Agency	Project	Allocation Date	Phase	Programmed Amount	Completed Allocations	Balance	Comments
TIFID	Agency	Froject	Date	riiase	Amount	Allocations	Dalalice	Comments
SOL990001	Caltrans	Route 80/680 Cordelia Auxiliary Lanes		CON & CON SUP	14,760,000	11,860,000	2,900,000	CON 14,300,000; CON SUP 460,000 This allocation splits off two landscaping project for delivery in FY 2003-04 and 2005- 06
SOL010030	Capitol Corr	J Bahia Viaduct Track Upgrade		PSE	190,000	0	190,000	*On CTC pending allocation list; below current allocation plan line - allocation not anticipated in near future. ENV 40,000; PSE 150,000
TOTALS FOR			14,950,000	11,860,000	3,090,000			

STIP ALLOCATION STATUS REPORT ALLOCATION DEADLINE 6/30/2003 SONOMA COUNTY

SONOMA COUNTY RTIP

TIP ID	Agency	Project	Allocation Date	Phase	Programmed Amount	Completed Allocations	Balance	Comments
	July							
								Allocated
			F	& WOS				(Caltrans Support)
				ROW			1	ROW 1,100,000; ROW SUP
SON950005	Caltrans	HOV, Wilfred-Santa Rosa	7/1/2002 S	SUP	1,800,000	1,800,000	0	700,000
								Allocated *Scope decreased
							· ·	rom 15 to 7 soundwalls.
			_,,					\$1.140M returned to Sonoma
SON991065	Caltrans	Soundwalls, Wilfred-Rt 12	6/26/2003 C		4,740,000	3,600,000	1,140,000	county share
			_	CON &				
	.		-	CON			_	
SON990003	Caltrans	Park/Ride, Rohnert Park interch	5/22/2003 S		225,000	225,000		Allocated
SON990001	Caltrans	HOV lanes, Rt 12-Steele Lane	7/1/2002 F		1,030,000	1,030,000	0 /	Allocated
				ROW				
SON010001	Caltrans	Steele Lane Interchange Improv	7/1/2002 S		118,000	118,000	0 /	Allocated
MTC990003	MTC	Regional rideshare program (SO)	9/17/2002 C	_	177,000	177,000	0 /	Allocated
MTC990005	MTC	PPM (SO)	9/16/2002 C	CON	31,000	31,000	0 /	Allocated
SON010017	SCTA	Planning, progr, and monitoring (SO)	7/18/2002 C	CON	235,000	235,000	0 /	Allocated
							;	\$1m will be returned to STIP
SON010024	SCTA	Rt 101 HOV lanes, Petaluma-Rohnert Park	8/22/2002 E	ENV	4,000,000	3,000,000	1,000,000	County Share
							;	\$1m will be returned to STIP
SON010025	SCTA	Rt 101 HOV lanes, Steele Ln-Windsor	8/22/2002 E	ENV	4,000,000	3,000,000	1,000,000	County Share
TOTALS FOR	TOTALS FOR SONOMA COUNTY 16,356,000 13,216,000 3,140,000							

ITIP

TOTALS FOR SONOMA COUNTY - ITIP
